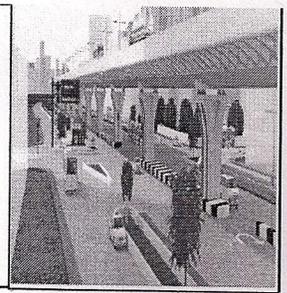


PROJECT MANAGER
FLYOVER PROJECT CIRCLE F-13
PUBLIC WORKS DEPARTMENT, GOVT. OF DELHI
MUKARBA CHOWK, G. T. KARNAL ROAD,
DELHI - 110033

Ph: 011-27691871, Fax No.: 011-27691971

E-Mail: pmpwddelhif13@gmail.com



F. No. 23(28-I)/PM/FPC/F-13/PWD/2014/ 1101

Date: - 19-5-14

Inspection Note


Sub: - Inspection Note for the work of "Comprehensive Development of Corridor (Outer Ring Road) between Madhuban Chowk to Mukarba Chowk".

Inspected the site of Madhuban Chowk to Mukarba Chowk today i.e. on 19.05.2014. and progress of work was reviewed with EE, F-131, his AEs and DPM of M/s. ITD. It was expressed that number of issues like desilting of drain, connection of road with new drain, removal of malba, cleaning of barricading boards, lightening of barricading boards etc. are not being taken care of. EE was directed to take immediate necessary action and issue notice to the contractor and get the work done at its risk & cost, if the agency fails to act in time.

The program of construction was discussed in detail with EE, F-131 and his AEs. EE, F-131 was directed to prepare a detailed program of execution and submit the same after discussion with the agency and this program should be enforced strictly.


The various resources like pier shutter, launchers for spine erection, cantilever frames for wing erection etc. should be procured by the agency on priority and strict monitoring by EE, F-131 should be done to ensure the above procurement.

Shifting of service by NDPL is going on at very slow pace. The matter was discussed with Mr. H.C. Sharma of NDPL who promised to give the feedback after taking stock of the latest position.


O/c Project Manager
Flyover Project Circle F-13, PWD

Copy to:-

- (1) Chief Engineer, Flyover Project Zone F-1, PWD, 12th Floor, MSO Building, I.P. Estate, New Delhi for kind information please.
- (2) The Executive Engineers, FPD, F-131 for information & necessary action please.


O/c Project Manager
