


**PROJECT MANAGER
FLYOVER PROJECT CIRCLE F-13
PUBLIC WORKS DEPARTMENT, GOVT. OF DELHI
MUKARBA CHOWK, G. T. KARNAL ROAD,
DELHI - 110033**

**Ph: 011-27691871, Fax No.: 011-27691971
E-Mail: pmpwddelhi13@gmail.com**

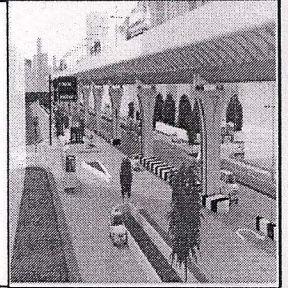


F. No. 23(29-I)/PM/FPC/F-13/PWD/2014/1195

Date: - 24-5-14

Inspection Note



Sub: - Inspection Note for the work of "Comprehensive Development of Corridor (Outer Ring Road) between Vikaspuri to Meera Bagh."

Inspected the site of Vikaspuri to Meerabagh and took the round of site starting from Janakpuri on 28.05.2014. Then reviewed the progress of work with Mr. Sengupta & Mr. Pal of M/s. Simplex and EE, F-132. Position of labour and steel reinforcement is still critical and the agency was not able to commit anything at the time. It was directed them to submit a detailed program of completion of work and EE, F-132 was directed to monitor the same accordingly. Required number of mould for wing casting and cantilever frames for erection of wings is very critical activity to be closely monitored by EE.


**Project Manager
Flyover Project Circle F-13, PWD**

Copy to:-

- (1) Chief Engineer, Flyover Project Zone F-1, PWD, 12th Floor, MSO Building, I.P. Estate, New Delhi for kind information please.
- (2) The Executive Engineers, FPD, F-132 for information & necessary action please.



Project Manager
