


PROJECT MANAGER
FLYOVER PROJECT CIRCLE F-13
PUBLIC WORKS DEPARTMENT, GOVT. OF DELHI
MUKARBA CHOWK, G. T. KARNAL ROAD,
DELHI - 110033

Ph: 011-27691871, Fax No.: 011-27691971

E-Mail: pmpwddelhif13@gmail.com

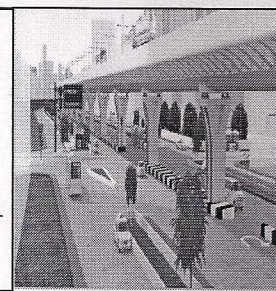

F. No. 23(23) (I)/PM/FPC/F-13/PWD/2014/1564

Date: - 7-7-14

Inspection Note

Name of work: - Comprehensive Development of Corridor (Outer Ring Road) between Mukarba Chowk to Wazirabad Chowk.

Inspected the site of Mukarba Chowk to Wazirabad along with EE, F-133, his AEs and Project Manager of M/s. CEC on 05.07.2014. First, visited the site of Bhalswa Bridge, Mukundpur Bridge and Burari Bridge where position of construction of bell mouth junction of main road with bridge were explored. Marking of various points of the bell mouth was done and it was felt that contractor should immediately start the work of widening in bell mouth and retaining wall will be required in only very small length at these locations. Regarding Mukundpur Chowk, it was directed to get the drawings of bell mouth junction superimposed on the GAD drawings showing the location of pier/portal frame of loop-1.

Then went to Jagatpur flyover and finalized the details of structures to be constructed at the junction of parallel road with Jagatpur road. It was felt that after blocking the drain, cast-in-situ culvert/drain may be constructed. Details of other structures, at this location to maintain the system of drainage during rainy season, as constructed by Irrigation & Flood Control Department, was also finalized.


From there, went to the site of solid slab casted in the Signature Bridge Project to see the finish of surface.

Then went to the PWD site office and reviewed the progress of earth work with Project Manager of M/s. CEC. It was pointed out that the supply of earth /fly ash should be immediately enhanced by the agency and work should be done at different junctions simultaneously. Project Manager of M/s. CEC informed that they are intending to complete the widening of Burari Junction first, then Bhalswa and then Mukundpur. He also informed that they are intending to complete whole widening work by Jan' 2015. The Project Manager was directed to prepare a detailed program of embankment widening work, along with details of required quantities of earth/fly ash immediately.


Project Manager
Flyover Project Circle F-13, PWD

Copy to:-

- (1) Chief Engineer, Flyover Project Zone F-1, PWD, 12th Floor, MSO Building, I.P. Estate, New Delhi for kind information please.
- (2) The Executive Engineer, FPD, F-133 for information & necessary action please.


Project Manager
