


PROJECT MANAGER
FLYOVER PROJECT CIRCLE F-13
PUBLIC WORKS DEPARTMENT, GOVT. OF DELHI
MUKARBA CHOWK, G. T. KARNAL ROAD,
DELHI - 110033

Ph: 011-27691871, Fax No.: 011-27691971
E-Mail: pmpwddelhif13@gmail.com

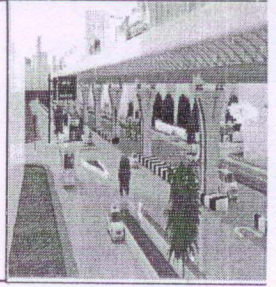

F. No. 23(28-I)/PM/FPC/F-13/PWD/2014/


1936

Date: - 20-8-14

Inspection Note


Sub: - Inspection Note for the work of "Comprehensive Development of Corridor (Outer Ring Road) between Madhuban Chowk to Mukarba Chowk" & "Comprehensive Development of Corridor (Outer Ring Road) between Mangolpuri to Madhuban Chowk".

Inspected the Dheerpur casting yard and discussed/reviewed the progress of work with Mr. Patil of M/s. ITD and EE, F-131 & F-134 on 14.08.2014. It was pointed out that various critical issues like casting of segments, erection of spine segments, erection of cantilever frames for wing erection need to be monitored closely to expedite the same. There are certain other issues like road widening/construction of footpath/construction of drain etc. where lot of scope is there which needs to be exploited by the agency to complete the whole project at an early date. The issue of procurement of second launcher was also discussed and Mr. Patil informed that they are going to procure one more overhead launcher for the stretch from Mangolpuri to Madhuban Chowk and for the other stretch from Madhuban Chowk to Mukarba Chowk, apart from overhead launcher, they will also be using two underslung launchers. Mr. Patil was advised that it will be better to procure the same at an early date rather than after delaying the work.


Project Manager
Flyover Project Circle F-13, PWD

Copy to:-

- (1) Chief Engineer, Flyover Project Zone F-1, PWD, 12th Floor, MSO Building, I.P. Estate, New Delhi for kind information please.
- (2-3) The Executive Engineer, FPD, F-131, F-134 for information & necessary action please.
- (4) File No. 23(24-I) for future reference please.


Project Manager
