


PROJECT MANAGER
FLYOVER PROJECT CIRCLE F-13
PUBLIC WORKS DEPARTMENT, GOVT. OF DELHI
MUKARBA CHOWK, G. T. KARNAL ROAD,
DELHI - 110033

Ph: 011-27691871, Fax No.: 011-27691971

E-Mail: pmpwddelhif13@gmail.com

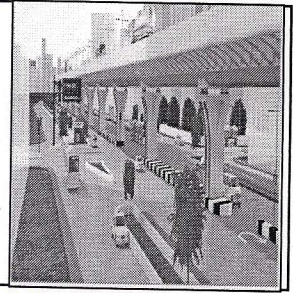

F. No. 23(24-I)/PM/FPC/F-13/PWD/2014/2317

Date: - 24.9.14

Inspection Note

Sub: - Inspection Note for the work of “Comprehensive Development of Corridor (Outer Ring Road) between Mangolpuri to Madhuban Chowk”.

Inspected the site of Mangolpuri to Madhuban Chowk along with EE, F-134 and Project Manager of M/s. ITD on 19.09.2014. First went to the site of Mangolpuri to Madhuban Chowk and inspected the pier, P-1 where bearing was being installed after using wedge-plate. Still the same was not fully adjusted as uneven gap was visible on four corners.

Then, went to the casting yard at Peeragarhi and reviewed the casting of wing segment. In the diaphragm wing segment, some problem of concrete not reaching below the sheathing duct towards expansion joint direction was reviewed. Few suggestions to be adopted during pouring were made and it was directed to give feedback after following the same. Some modifications in the shuttering arrangement of wing form work, having dowels in vertical direction to become part of longitudinal stitching, were made so as to avoid leakage of slurry and have a better surface of concrete. It was directed to immediately do the necessary rectification in time bound manner and EE, F-134 was directed to ensure the same. It was also directed to ensure proper curing of wing segments.


Then, in the lab, witnessed the testing of M-60 7 day's cubes and results were found to be satisfactory.


Project Manager
Flyover Project Circle F-13, PWD

Copy to:-

- (1) Chief Engineer, Flyover Project Zone F-1, PWD, 12th Floor, MSO Building, I.P. Estate, New Delhi for kind information please.
- (2) The Executive Engineer, FPD, F-134 for information & necessary action please.

(3) EEF-131 for information and n. a. pl.


o/e Project Manager
