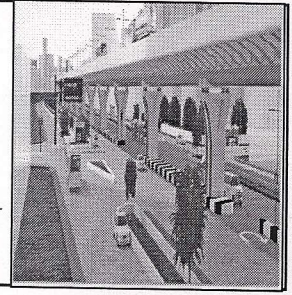


PROJECT MANAGER
FLYOVER PROJECT CIRCLE F-13
PUBLIC WORKS DEPARTMENT, GOVT. OF DELHI
MUKARBA CHOWK, G. T. KARNAL ROAD,
DELHI - 110033

Ph: 011-27691871, Fax No.: 011-27691971

E-Mail: pmpwddelhif13@gmail.com



F. No. 23(29-I)/PM/FPC/F-13/PWD/2014/ 2330

Date: - 24-9-14

Inspection Note

Sub: - Inspection Note for the work of "Comprehensive Development of Corridor (Outer Ring Road) between Vikaspuri to Meera Bagh."

Inspected the site of Vikaspuri to Meerabagh along with EE, F-132 and Project Manager of M/s. Simplex on 23.09.2014. First inspected the span where wing erection has been completed and alignment was being done. It was directed that concrete surface of spine & wing should be properly cleaned/hacked & nitobond applied on concrete surface before stitch concrete. It was also directed that alignment should be thoroughly checked to ensure that the desired profile is achieved.

It was observed that number of barricading boards placed near A-2 RE wall and other locations are damaged and should be immediately replaced. This has already been pointed out earlier.


Some repair of DJB line was being done near A-2 pier on R.H.S and EE, F-132 was directed to place the levelling course of concrete between the old road and new surface road as there is a large level difference and traffic movement should be made smooth.

The status of removal of malba, cleaning and painting of barricading boards was also enquired. EE informed that painting of barricading boards has been started at some locations and activity of malba removal is also in progress and EE was directed to closely monitor these issues and take necessary action at the risk and cost of the agency, if it does not perform in a desired manner promptly.

Then, went to the location of second launcher where threading of strands was in progress.


Then, went to casting yard and reviewed the progress of spine and wing casting. It is felt that labour for casting of spine and wings needs to be increased drastically. Curing arrangements at site should be regularly monitored to ensure regular and adequate curing.

Then, took the round of casting yard and understood the new arrangement for casting of diaphragm wing segment, being proposed, to ensure proper flow of concrete in all directions.


Project Manager
Flyover Project Circle F-13, PWD

Copy to:-

- (1) Chief Engineer, Flyover Project Zone F-1, PWD, 12th Floor, MSO Building, I.P. Estate, New Delhi for kind information please.
- (2) The Executive Engineers, FPD, F-132 for information & necessary action please.


Project Manager
