


PROJECT MANAGER
FLYOVER PROJECT CIRCLE F-13
PUBLIC WORKS DEPARTMENT, GOVT. OF DELHI
MUKARBA CHOWK, G. T. KARNAL ROAD,
DELHI - 110033

Ph: 011-27691871, Fax No.: 011-27691971
E-Mail: pmpwddelhi13@gmail.com

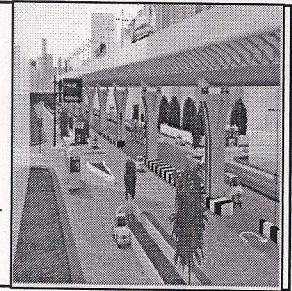

F. No. 23(24-I)/PM/FPC/F-13/PWD/2014/ 2477


Date: - 13-10-14

Inspection Note

Sub: - Inspection Note for the work of "Comprehensive Development of Corridor (Outer Ring Road) between Mangolpuri to Madhuban Chowk".

Inspected the site of Mangolpuri to Madhuban Chowk along with EE, F-134 and Project Manager of M/s. ITD on 08.10.2014 and inspected where wing erection in first span is in progress. Various issues w.r.t. alignment of wing segments were discussed at site. It was pointed out that the fin of wing segment, touching the spine should be properly cleaned before erection and if during transportation/erection, this fin has been damaged/cracked, **it should be dismantled on priority**. The Reinforcement in the stitch portion between wing to spine and wing to wing should be properly checked before allowing stitch concrete. Lot of problems are expected to be faced during re-baring and necessary modifications in the drawings may required to be made by the consultant as already discussed with him.

Then, EE showed certain locations where footpath work is being taken up and issues regarding the fixing of kerb stones and their height were decided at site, as per site situation. The issue of connection of drain after A-2 pier was also seen at site. At this location, a trunk drain is passing through a DDA park and it was advised that new drain should be connected with this trunk drain in coordination with DDA authorities.


10/10
% Project Manager
Flyover Project Circle F-13, PWD

Copy to:-

- (1) Chief Engineer, Flyover Project Zone F-1, PWD, 12th Floor, MSO Building, I.P. Estate, New Delhi for kind information please.
- (2) The Executive Engineer, FPD, F-134 for information & necessary action please.


13/10
% Project Manager
