


**PROJECT MANAGER
FLYOVER PROJECT CIRCLE F-13
PUBLIC WORKS DEPARTMENT, GOVT. OF DELHI
MUKARBA CHOWK, G. T. KARNAL ROAD,
DELHI - 110033**

Ph: 011-27691871, Fax No.: 011-27691971

E-Mail: pmpwddelhif13@gmail.com

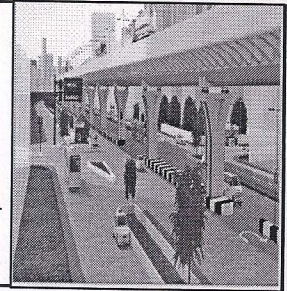

F. No. 23(23) (I)/PM/FPC/F-13/PWD/2014/

2751

Date: - 14-11-14

Inspection Note

Name of work: - Comprehensive Development of Corridor (Outer Ring Road) between Mukarba Chowk to Wazirabad Chowk.

Inspected the site of M/s. CEC from Mukarba Chowk to Wazirabad with Project Manager of M/s. CEC, Mr. Hemendra Chaudhry of M/s. ITD doing the piling work and EE/F-133 & his AEs on 13.11.2014. First, inspected the site of Libaspur Bridge where piling work is in progress. The methodology of completing the piling work and pile cap work was discussed in detail.

Then, went to the site of P-22 pier of loop-2, where work is held up because of interceptor sewer work. It was pointed out that most probably DJB will be giving the clearance on coming Friday but the pile and pile cap work at this location is to be completed within one month as committed to DJB authorities, after receipt of NOC from DJB. Therefore, the agency should take advance action to make preparation for doing the job of pile, pile cap of P-22 so that once the clearance is received, no time is wasted. Approach for piling rig, transit mixtures was also seen. The piling agency agreed to execute this work, after receipt of clearance from DJB, on priority.

Then, went to the Jagatpur flyover location where piling in rock is to be started from Monday. It was decided that he should start the piling work in PR-6 and PR-7 pile group. The matter was also discussed with Mr. Rajiv Shukla of M/s. LTR to find out the solution of either casting of span in stages or pre-stressing in stages, because as per the present drawings, there is one module of P-3, P-4, P-5, P-6 which covers the entire width of nallah. During casting and pre-stressing in one stage, water diversion will be a big issue. After detailed discussion, Mr. Shukla suggested that they may look for suggesting pre-stressing in stage. He committed to come to site on Monday. Also, discussed the issue of road widening of road going to Jagatpur Village on R.H.S. where culvert has already been completed. It was also decided to construct the small wing walls and do the filling over culvert so that road widening is completed on R.H.S. up to 50 m and pile work of pile groups on both sides of 220 KVA HT lines is started. DPM of M/s. CEC committed that within next 15 days, this road widening work will be completed. The issue of drainage on R.H.S. was also discussed in detail and scheme was finalized and explained to M/s. CEC and EE, F-133.

[Signature]
o/c Project Manager
Flyover Project Circle F-13, PWD

Copy to:-

- (1) Chief Engineer, Flyover Project Zone F-1, PWD, 12th Floor, MSO Building, I.P. Estate, New Delhi for kind information please.
- (2) The Executive Engineer, FPD, F-133 for information & necessary action please.

[Signature]
o/c Project Manager
