


PROJECT MANAGER
FLYOVER PROJECT CIRCLE F-13
PUBLIC WORKS DEPARTMENT, GOVT. OF DELHI
MUKARBA CHOWK, G. T. KARNAL ROAD,
DELHI - 110033

Ph: 011-27691871, Fax No.: 011-27691971

E-Mail: pmpwddelhif13@gmail.com

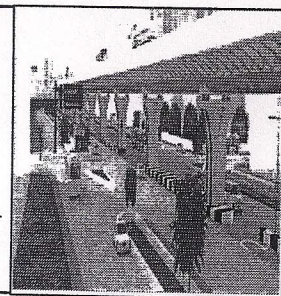

F. No. 23(24-I)/PM/FPC/F-13/PWD/2014/ 2967

Date: - 8-12-14

Inspection Note

Sub: - Inspection Note for the work of "Comprehensive Development of Corridor (Outer Ring Road) between Mangolpuri to Madhuban Chowk".

Inspected the site of Mangolpuri to Madhuban Chowk along with EE, F-134 and Project Manager of M/s. ITD on 08.12.2014. One sample of stitch concrete using the PVC shutter has been casted and surface was observed to be O.K. Also the shutter for casting of shear blocks, shear resistor was being placed at one location. It was directed to do the one sample of each so that it is started at other locations in full swing. It was again directed that the finishing work of erected spine and wing segments should be started from one end as it may be time consuming activity. The RE wall work on A-1 side was in progress. EE was directed to regularly check the quality of sand to ensure its suitability for RE wall work.

Then, went to the A-2 side, where road widening work is in progress. There was some leakage from DJB pipeline and EE intimated that he has contacted the DJB officials for necessary rectification.

In the site office, reviewed the various issues including location of piles for FOBs. At foundation locations of both FOBs near Mangolpuri flyover and Deepali Chowk, DJB pipelines are running and therefore the piles in these areas are to be rearranged as per site condition and got designed from consultant. EE was directed to finalize the same on top priority.

The issue of maintenance of roads and deployment of marshals were also discussed in detail. It was directed that as a daily routine, contractor's Engineers should inspect the whole stretch on both sides to ascertain that there is no pot-holes and, if found, it should be repaired on top priority. Sufficient marshals should be deployed at intersections/U-turns to regulate the traffic as in the recent past, huge traffic jams has been noticed at various places. In the night, proper illumination of site as well as barricading boards should also be ensured.

de 8/12
Project Manager

Flyover Project Circle F-13, PWD

Copy to:-

- (1) Chief Engineer, Flyover Project Zone F-1, PWD, 12th Floor, MSO Building, I.P. Estate, New Delhi for kind information please.
- (2) The Executive Engineer, FPD, F-134 for information & necessary action please.

de 8/12
Project Manager
