


PROJECT MANAGER
FLYOVER PROJECT CIRCLE F-13
PUBLIC WORKS DEPARTMENT, GOVT. OF DELHI
MUKARBA CHOWK, G. T. KARNAL ROAD,
DELHI - 110033

Ph: 011-27691871, Fax No.: 011-27691971

E-Mail: pmpwddelhif13@gmail.com

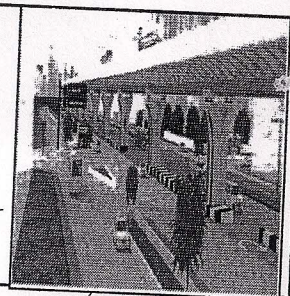

F. No. 23(29-I)/PM/FPC/F-13/PWD/2014/ **3120**

Date: - **29-12-14**

Inspection Note

Sub: - Inspection Note for the work of "Comprehensive Development of Corridor (Outer Ring Road) between Vikaspuri to Meera Bagh."

Inspected the site of Vikaspuri to Meerabagh along with Executive Engineer, F-132 and DPM of M/s. Simplex on 29.12.2014. Preparation for casting of central verge crash barrier, in the span where wing segments have been erected was in progress. The methodology for providing cross-drainage pipe for drainage of water from one side to other side was discussed in detail.

Then, went to the nallah portion, where on R.H.S., reinforcement for one pile cap was in progress, which was reviewed.

Thereafter, took the round of the site and went to the casting yard. At one location, after PVR Sonia on L.H.S., Kerb stones were being fixed for footpath. It was directed to ensure that kerb stones are properly placed so as to have a finished height of footpath as 150 mm from finished road level. The kerb stones should be properly fixed with grooves formed. The kerb stones were also being casted near CRPF Red Light. It was directed to make arrangement of sufficient water for curing of kerb stones and thickness of the kerb stones should be properly maintained.

In the casting yard, reviewed the progress of casting and erection of spine & wing segment. It is felt that still more labour deployment is required to enhance the progress of casting of spines and wings. Wing casting has become very critical and agency should immediately take necessary action, in this regard. The speed of wing erection is also going on very slow as at least with one set, two spans should be erected, which is not the case.

With regard to cleaning of site, a lot is still required to be done by the agency and EE was directed to immediately take necessary action at the risk & cost of the agency.

Copy to:-

- (1) Chief Engineer, Flyover Project Zone F-1, PWD, 12th Floor, MSO Building, I.P. Estate, New Delhi for kind information please.
- (2) The Executive Engineers, FPD, F-132 for information & necessary action please.

Project Manager
Flyover Project Circle F-13, PWD

Project Manager
